


TENTATIVE TIMELINE*

The Project is planned to be divided into three main phases of operation in order to reduce community impact.

NOTICE OF PREPARATION (NOP)

Notice of Preparation (NOP) prepared to seek input from local agencies and the public regarding the scope and content of the environmental information to be included in the Draft Program Environmental Impact Report (PEIR)

2023

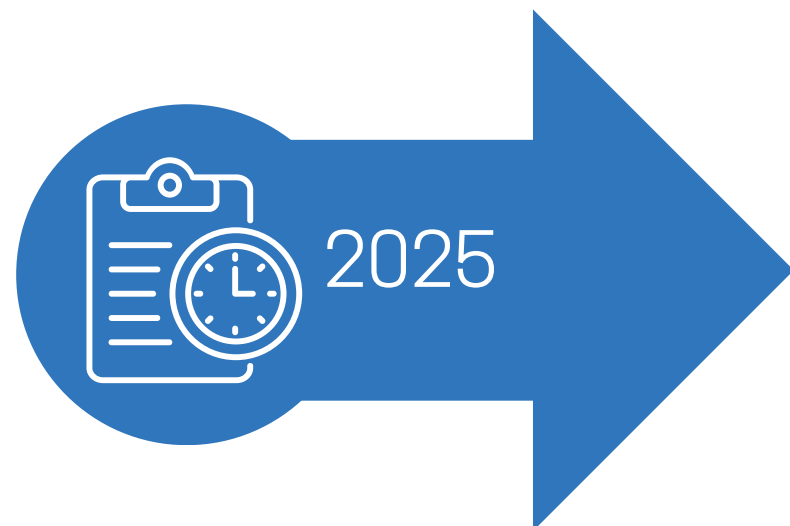

2025

DRAFT PROGRAM ENVIRONMENTAL IMPACT REPORT

1. Draft PEIR prepared. Upon completion, Public Works will file a Notice of Completion (NOC) and give public notice of availability of Draft PEIR.
2. Public and agency review of Draft PEIR (min. 45 days review period)
3. Final PEIR prepared including responses to comments on the Draft PEIR.

BOARD OF SUPERVISORS REVIEW

Final PEIR and Project Approval under consideration by Board of Supervisors

2026



LATE
2027


PHASE 1: SITE PREPARATION / CONSTRUCTION BEGINS

An access road from Little Tujunga Canyon Road to the Reservoir will be restored.

PHASE 1: SEDIMENT REMOVAL BEGINS

- Up to 1.5 million cubic yards of sediment will be removed over the course of 5 years or less.
- There will be controlled releases of water into Pacoima Wash, before the sediment is then excavated and trucked to nearby landfills or gravel pits

2028

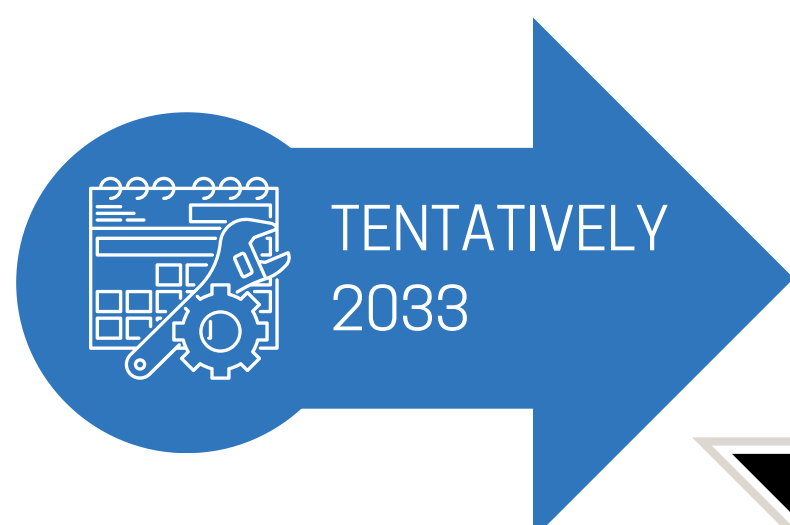

TENTATIVELY
2033

PHASE 2: CONSTRUCTION BEGINS

- An additional 2.2-4 million cubic yards of sediment will be removed over the course of 10 years or less.
- Sediment will be moved by either trucks and/or a conveyor belt system.

PHASE 3: LONG TERM MAINTENANCE

A long-term maintenance plan will be implemented in order to reduce the need for further large-scale sediment-removal projects such as this one.

***Note: These dates are all subject to change**
