

MAP  
OF  
VENTURA ROAD  
AT  
SYCAMORE CREEK  
IN  
CALABASAS ROAD DISTRICT

DEC. 1912 IVORY B. NOBLE COUNTY SURVEYOR.

FIELD WORK H.E.W.  
OFFICE WORK Jones  
CHECKED BY H.E.W.

SHOWING LOCATION OF 6 FOOT ARCH


CS	7	8	3	3
A	1	OF	A	2

# GRADE SHEET FOR CULVERT ON VENTURA ROAD SYCAMORE CREEK

Scale: 1"=4'

L.B. 63-50

FIELD WORK... H.E.W.  
OFFICE WORK... *Bowling*  
CHECKED BY... H.E.W.

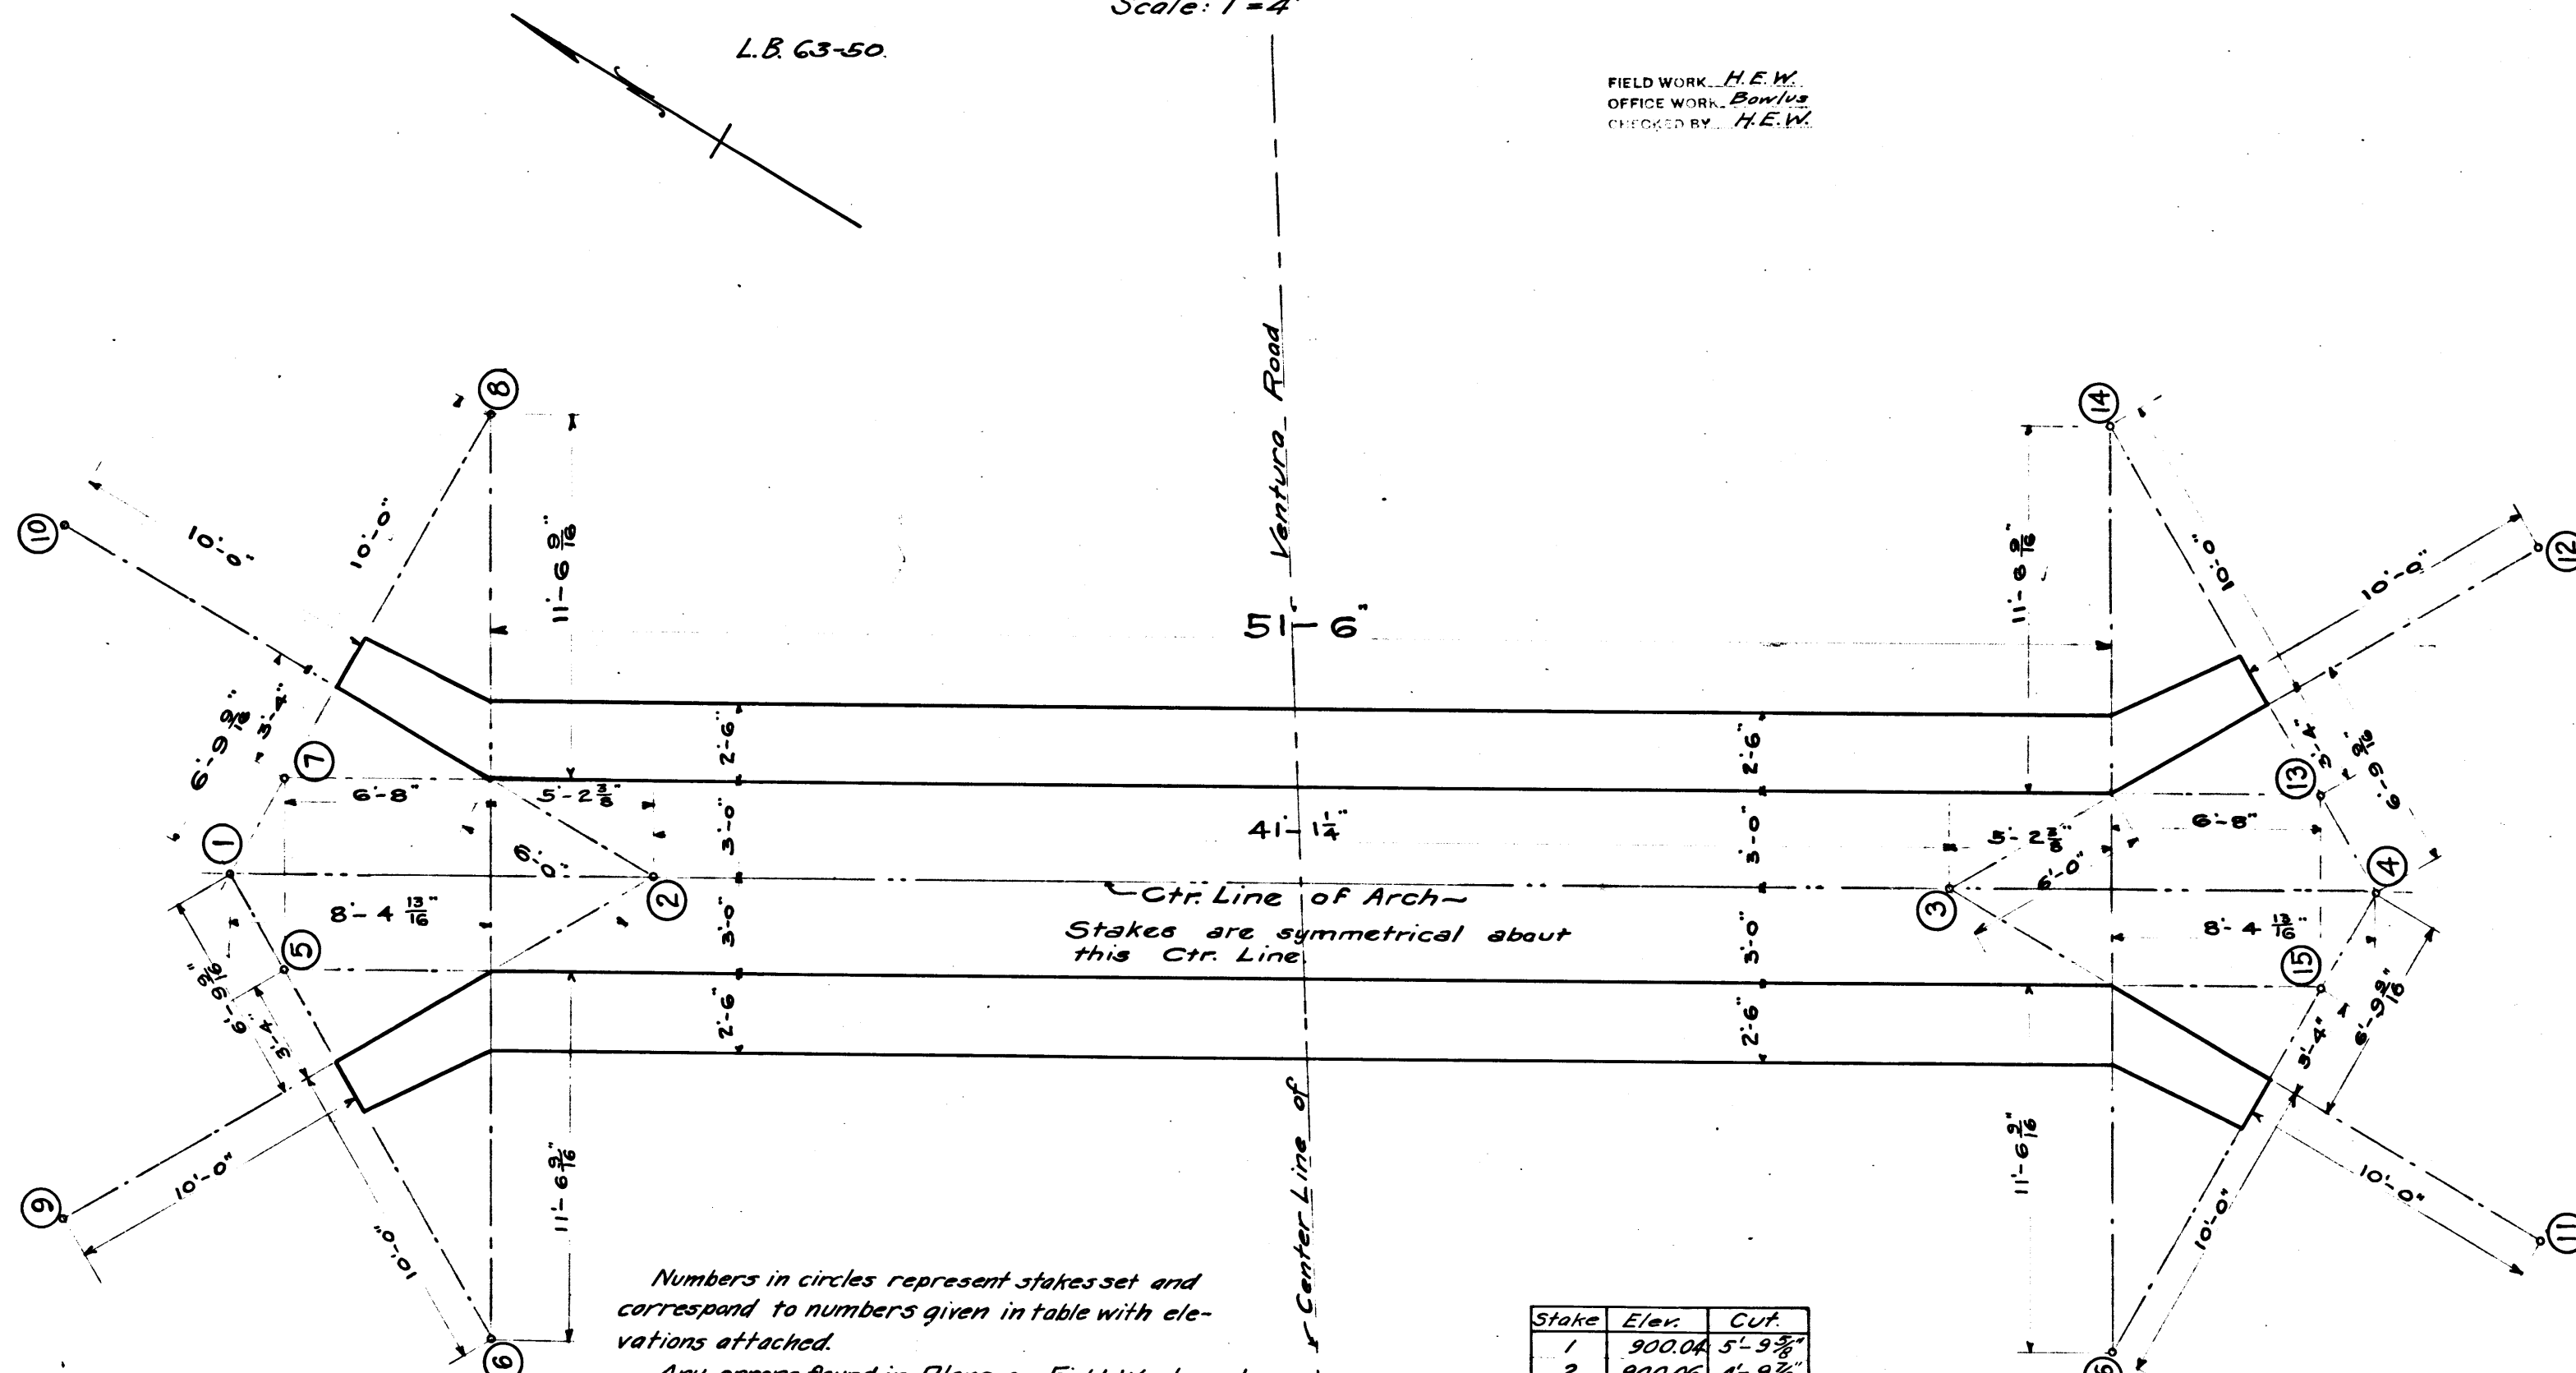

Numbers in circles represent stakes set and correspond to numbers given in table with elevations attached.

Any errors found in Plans or Field Work must be reported to the County Surveyor at once.

All grades for excavations, and elevations for finished work of culvert are to be taken from the nearest stake shown on this sheet and grades so established checked with stakes near same.

Cuts are to bottom of footings for wing walls and bottom of abutments of arch. Cuts given for stakes 1, 5, 6, 7, 8, 9 & 10 are to bottom of footings of wing walls which at this end is one foot lower than bottom of arch abutments.

All cuts refer to bottom of footings at Ends of arch.

Stake	Elev.	Cut.
1	900.04	5'-9 3/8"
2	900.06	4'-9 7/8"
3	900.33	4'-6 7/8"
4	900.42	4'-7 7/8"
5	900.04	5'-9 3/8"
6	907.27	13'-0 3/8"
7	900.07	5'-10"
8	905.18	10'-11 1/2"
9	907.36	13'-1 1/2"
10	902.73	8'-5 7/8"
11	903.68	7'-11"
12	903.26	7'-6"
13	901.78	6'-0 1/4"
14	905.76	10'-0"
15	900.36	4'-7 1/4"
16	905.97	10'-2 1/2"

CS 7833

A 2 OF A 2

