TASK	DAYS	START	FINISH
Olive View - UCLA			
AGENCY APPROVAL - PLAN CHECK			
OSHPD Plan Check Review	0	19FEB04A	13AUG04A
A&E Incorporate OSHPD comments	0*	16AUG04A	29OCT04A
A&E Incorporate NPC3 Areas.	0*	16AUG04A	29OCT04A
OSHPD Backcheck	0	01NOV04A	25JAN05A
OSHPD Stamp Approval	0	25JAN05A	
OSHPD Construction Permit	21	28FEB06	28MAR06
BID & AWARD			
B.o.S.#1 (Adopt 90% CDs)			
File, Adopt & Advertise Board Letter	1	25AUG05	25AUG05
Board Action	1	06SEP05	06SEP05
Advertise Project	1	07SEP05	07SEP05
B.o.S.#2 (Pre-Qual., 100% CDs, Conslt. Cont.)			
AED to Prepare General Conditions for Bid	64	13DEC04A	17NOV05
File, Adopt & Adv. Approved Dwgs. & Cont. list	1	17NOV05	17NOV05
Board Action	1	06DEC05	06DEC05
Announce Final Qualified Contractor's List	1	07DEC05	07DEC05
Construction Bid Period	36	08DEC05	08FEB06
Evaluate Bids	2	09FEB06	13FEB06
Issue NTP (Consultant Agreement)	0	28FEB06	
B.o.S.#3 (Award Construction Contract)			
File / Award Board Letter	1	30MAR06	30MAR06
Board Action	1	11APR06	11APR06
Award & Execute Contract	8	12APR06	25APR06
CONSTRUCTION			
CONSTRUCTION (overall phase)	686*	28FEB06	14JAN08
Consultant Agreement Work Period	90	28FEB06	28MAY06
Issue NTP (Construction)	0	29MAY06	
Construction Work (current plan)	534	30MAY06	14NOV07
Substantial Completion	0	15NOV07	
Punchlist & Project Close-out	61	15NOV07	14JAN08

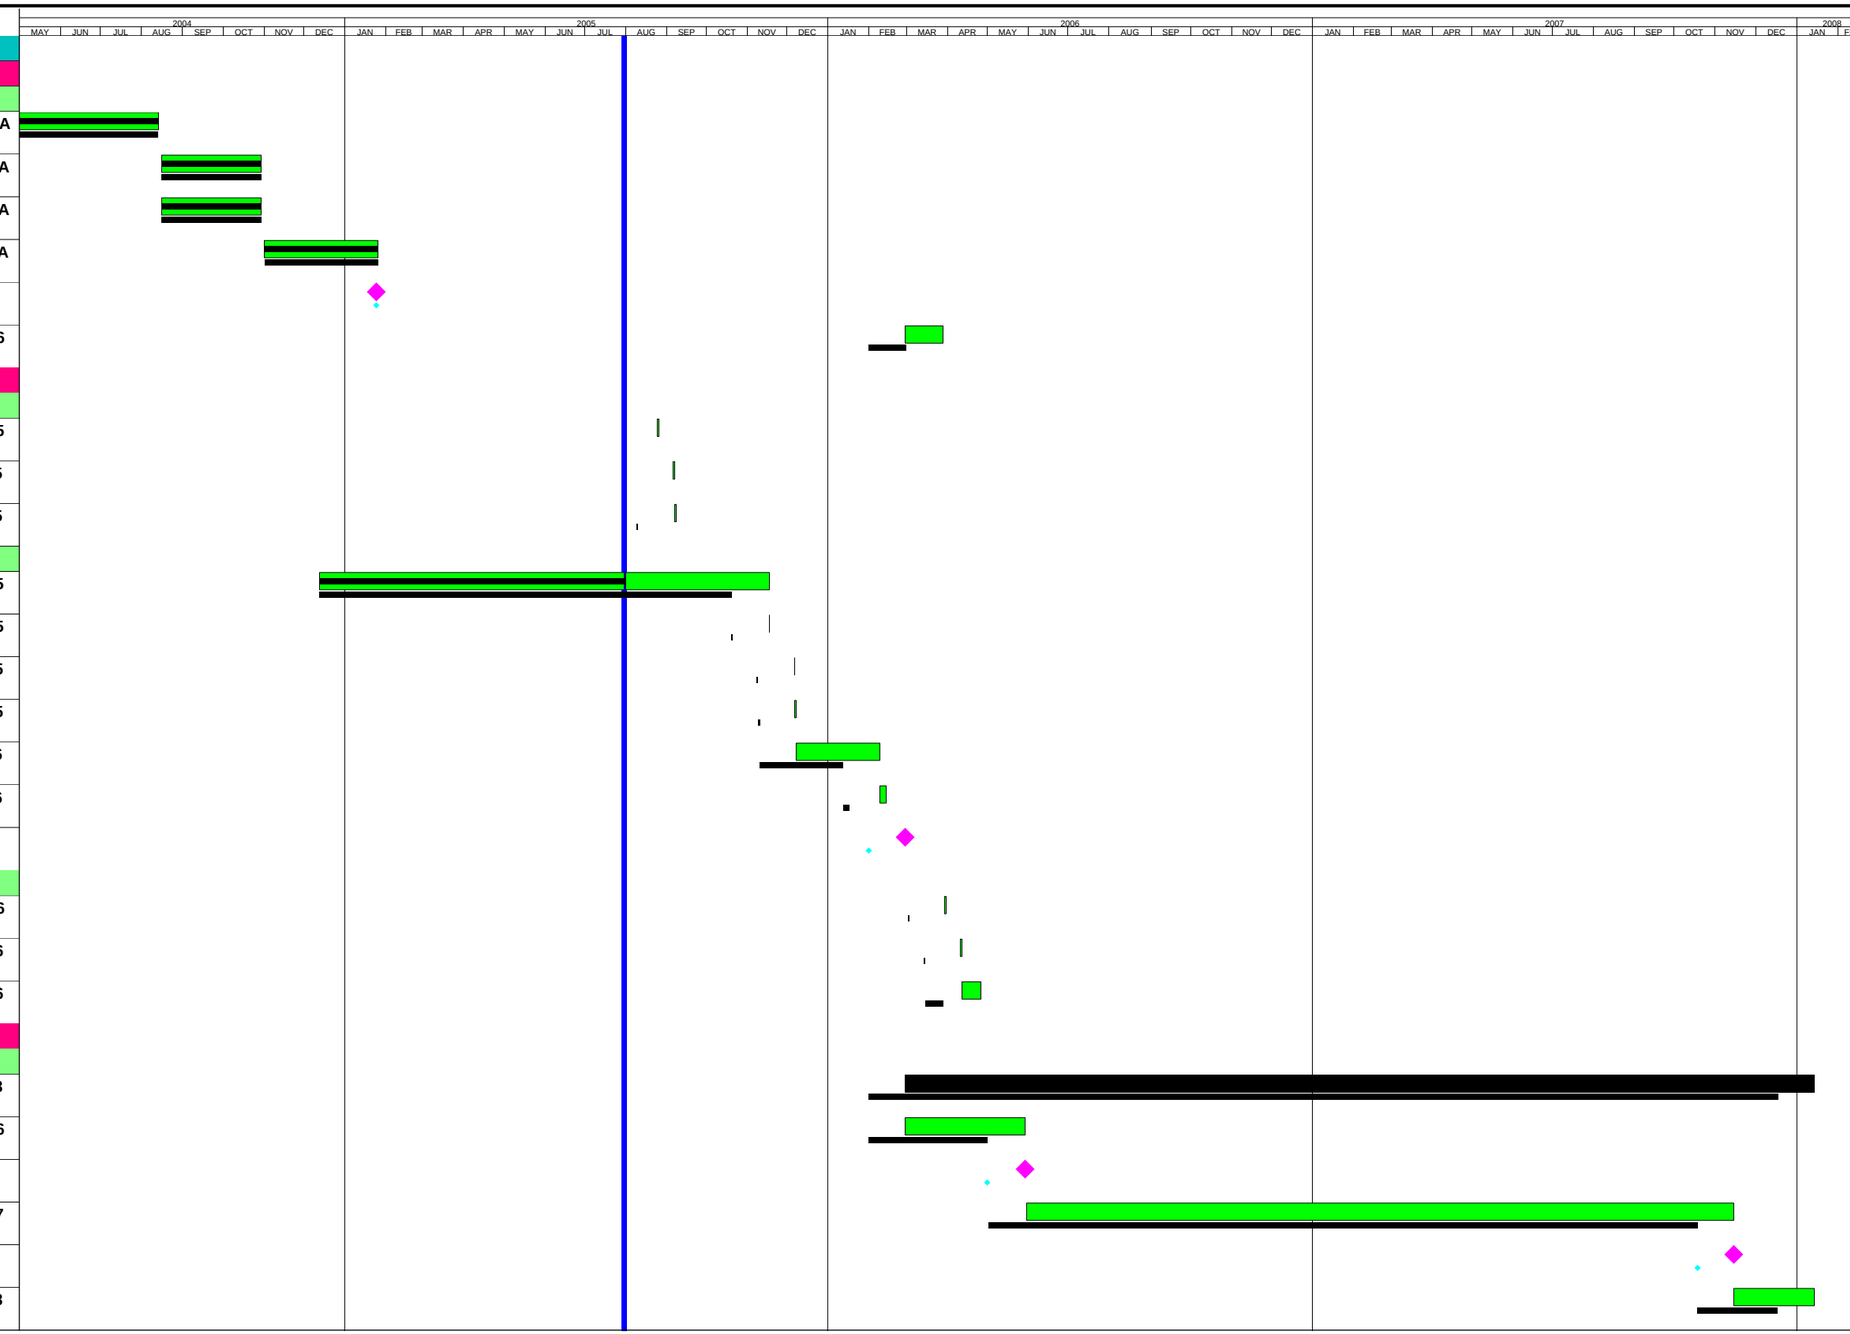

URS

COUNTY OF LOS ANGELES CALIFORNIA

© Primavera Systems, Inc.

SB1953

Project Update
OLIVE VIEW - UCLA

by S. Pogact

Date	Revision	Checked	Approved
25AUG05	July '05 update (31JUL05)		
02AUG05	June update (30JUN05)		
23JUN05	May update (31MAY05)		
