TASK	DAYS	START	FINISH
Harbor - UCLA			
AGENCY APPROVAL - PLAN CHECK			
OSHPD Plan Check Review	0	19MAY04A	03JAN05A
A&E Incorporate OSHPD comments +add'l NPC3 areas	0*	04JAN05A	02SEP05A
OSHPD Backcheck 1	71	06SEP05A	06JAN06
A&E Incorporate OSHPD comments	24	09JAN06	09FEB06
OSHPD Response- Backcheck 2	63	10FEB06	09MAY06
OSHPD Stamp Approval	0	10MAY06	
OSHPD Construction Permit	21	08AUG06	05SEP06
BID & AWARD			
B.o.S.#1 (Adopt 90% CDs + PreQual)			
File, Adopt & Advertise Board Letter	1	06OCT05*	06OCT05
Board Action	1	18OCT05*	18OCT05
Advertise Project	1	19OCT05	19OCT05
B.o.S. #2 (Adopt Contractor list)			
File + Adopt Contractor's list Board Letter	1	09FEB06	09FEB06
Board Action	1	28FEB06	28FEB06
Announce Final Qualified Contractor's List	0		28FEB06
B.o.S. #3 (Adopt 100% CDs)			
AED to Prepare General Conditions for Bid	42	30NOV05	09FEB06
File, Adopt & Adv. Approved Dwgs.	1	11MAY06	11MAY06
Board Action	1	23MAY06	23MAY06
(Consultant Agreement)			
Construction Bid Period	33	24MAY06	19JUL06
Evaluate Bids	2	20JUL06	24JUL06
Issue NTP (Consultant Agreement)	0	08AUG06	
B.o.S.#4 (Award Construction Contract)			
File / Award Board Letter	1	14SEP06	14SEP06
Board Action	1	26SEP06	26SEP06
Award & Execute Contract	8	27SEP06	10OCT06
CONSTRUCTION			
Consultant Agreement Work Period	151	08AUG06	05JAN07
Issue NTP (Construction)	0	08JAN07	
Construction Work (3 year plan)	1,096	08JAN07	07JAN10
Substantial Completion	0		07JAN10
CONSTRUCTION (overall phase)	1,310*	08AUG06	09MAR10
Punchlist & Project Close-out	61	08JAN10	09MAR10

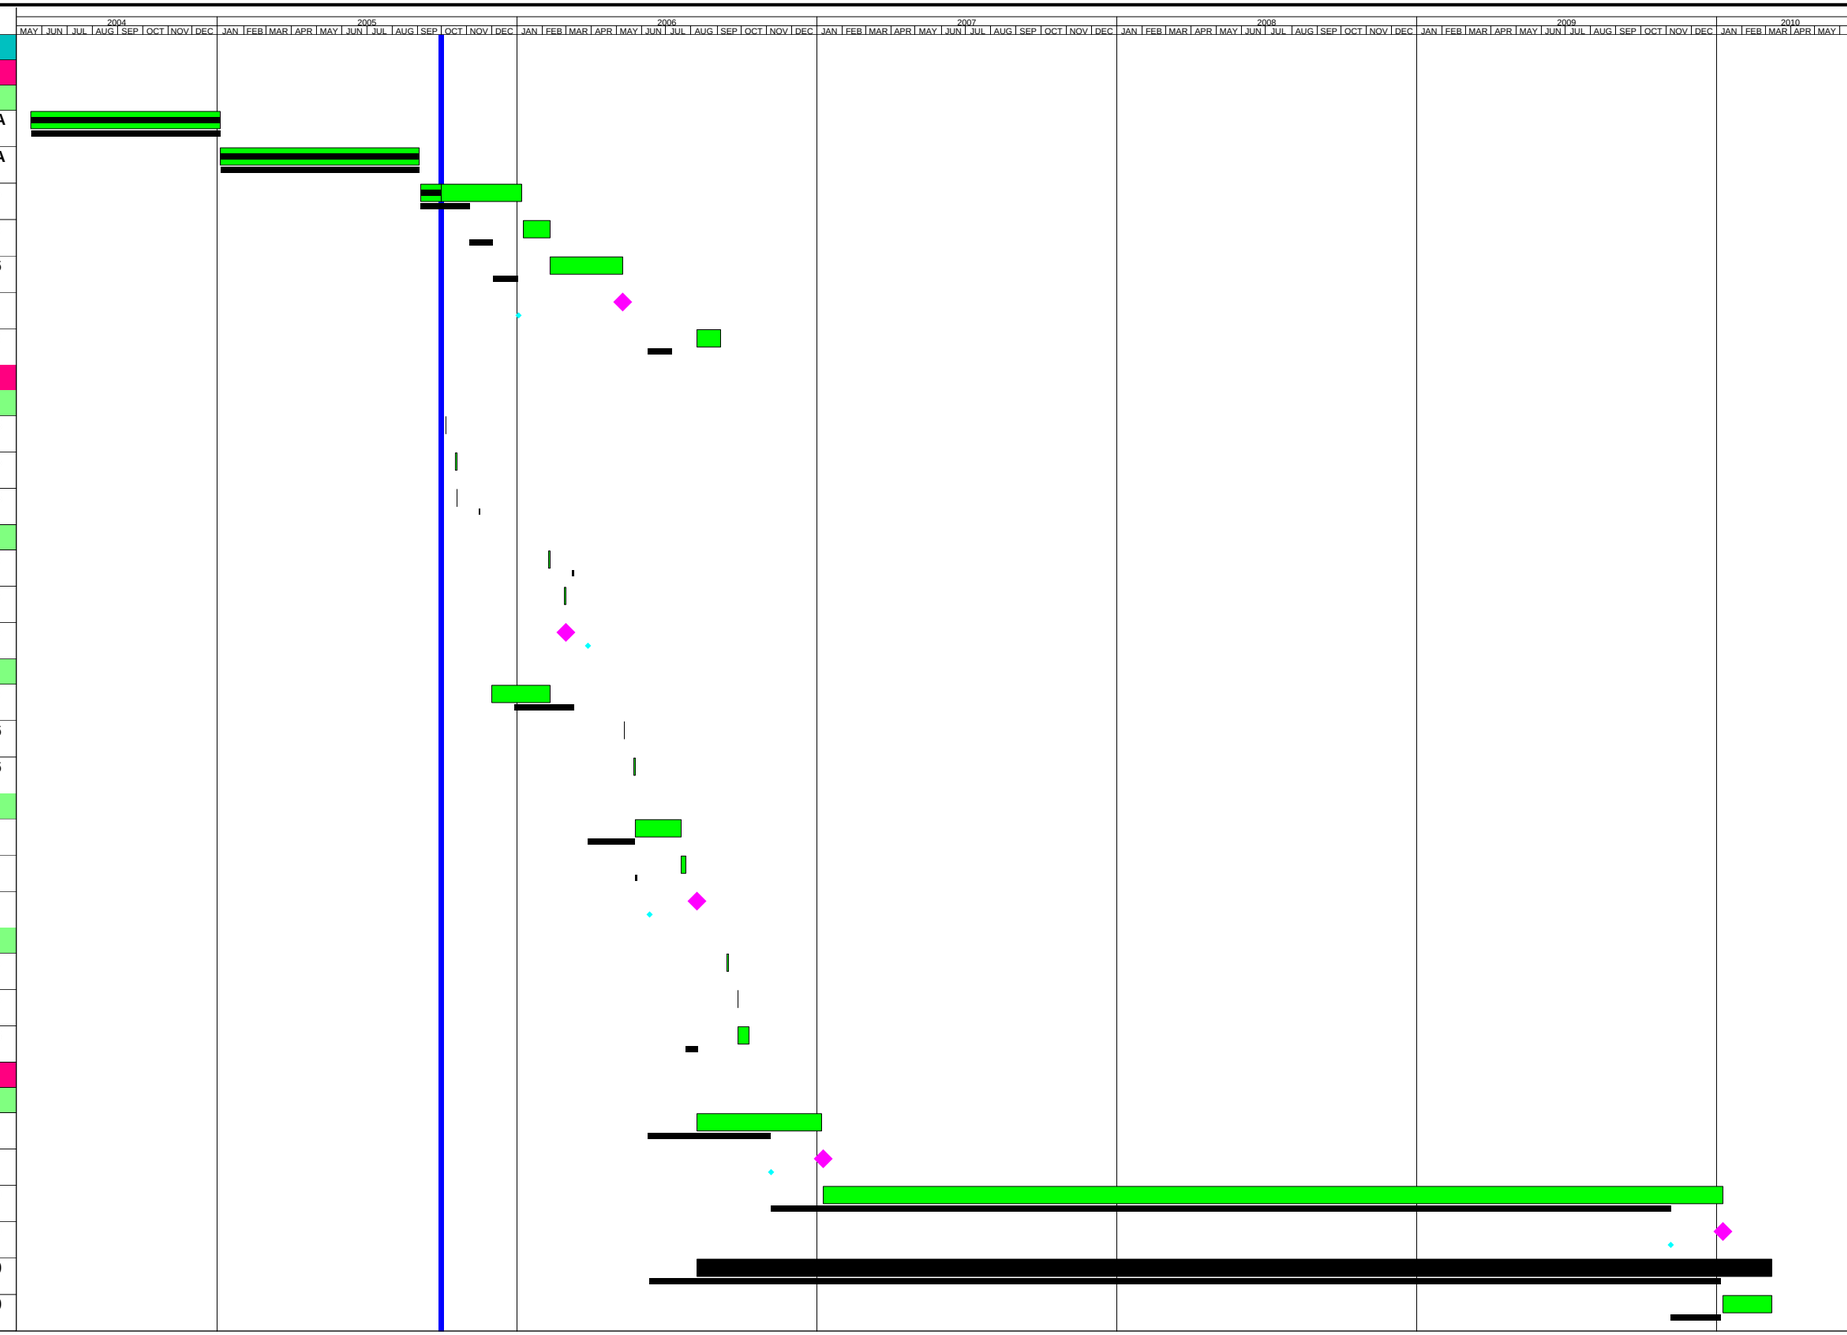

URS

© Primavera Systems, Inc.

SB1953

Project Update
HARBOR - UCLA

by S. Pogact

Date	Revision	Checked	Approved
13OCT05	September '05 update (30SEP05)		
28SEP05	August '05 update (31AUG05)		
25AUG05	July '05 update (31JUL05) (file board letter?)		
02AUG05	June update (30JUN05) DRAFT***		
23JUN05	May update (31MAY05)		
