TASK	DAYS	START	FINISH
Olive View - UCLA			
AGENCY APPROVAL - PLAN CHECK			
OSHPD Plan Check Review	0	19FEB04A	13AUG04A
A&E Incorporate OSHPD comments	0*	16AUG04A	29OCT04A
A&E Incorporate NPC3 Areas.	0*	16AUG04A	29OCT04A
OSHPD Backcheck	0	01NOV04A	25JAN05A
OSHPD Stamp Approval	0	25JAN05A	
OSHPD Construction Permit	21	25APR06	23MAY06
BID & AWARD			
B.o.S.#1 (Adopt 90% CDs)			
File, Adopt & Advertise Board Letter	1	20OCT05*	20OCT05
Board Action	1	01NOV05	01NOV05
Advertise Project	1	02NOV05	02NOV05
B.o.S.#2 (Pre-Qual., 100% CDs, Conslt. Cont.)			
AED to Prepare General Conditions for Bid	11	13DEC04A	19OCT05
File, Adopt & Adv. Approved Dwgs. & Cont. list	1	12JAN06	12JAN06
Board Action	1	31JAN06	31JAN06
Announce Final Qualified Contractor's List	1	01FEB06	01FEB06
Construction Bid Period	36	02FEB06	05APR06
Evaluate Bids	2	06APR06	10APR06
Issue NTP (Consultant Agreement)	0	25APR06	
B.o.S.#3 (Award Construction Contract)			
File / Award Board Letter	1	25MAY06	25MAY06
Board Action	1	06JUN06	06JUN06
Award & Execute Contract	8	07JUN06	20JUN06
CONSTRUCTION			
CONSTRUCTION (overall phase)	686*	25APR06	10MAR08
Consultant Agreement Work Period	90	25APR06	23JUL06
Issue NTP (Construction)	0	24JUL06	
Construction Work (current plan)	534	25JUL06	09JAN08
Substantial Completion	0	10JAN08	
Punchlist & Project Close-out	61	10JAN08	10MAR08

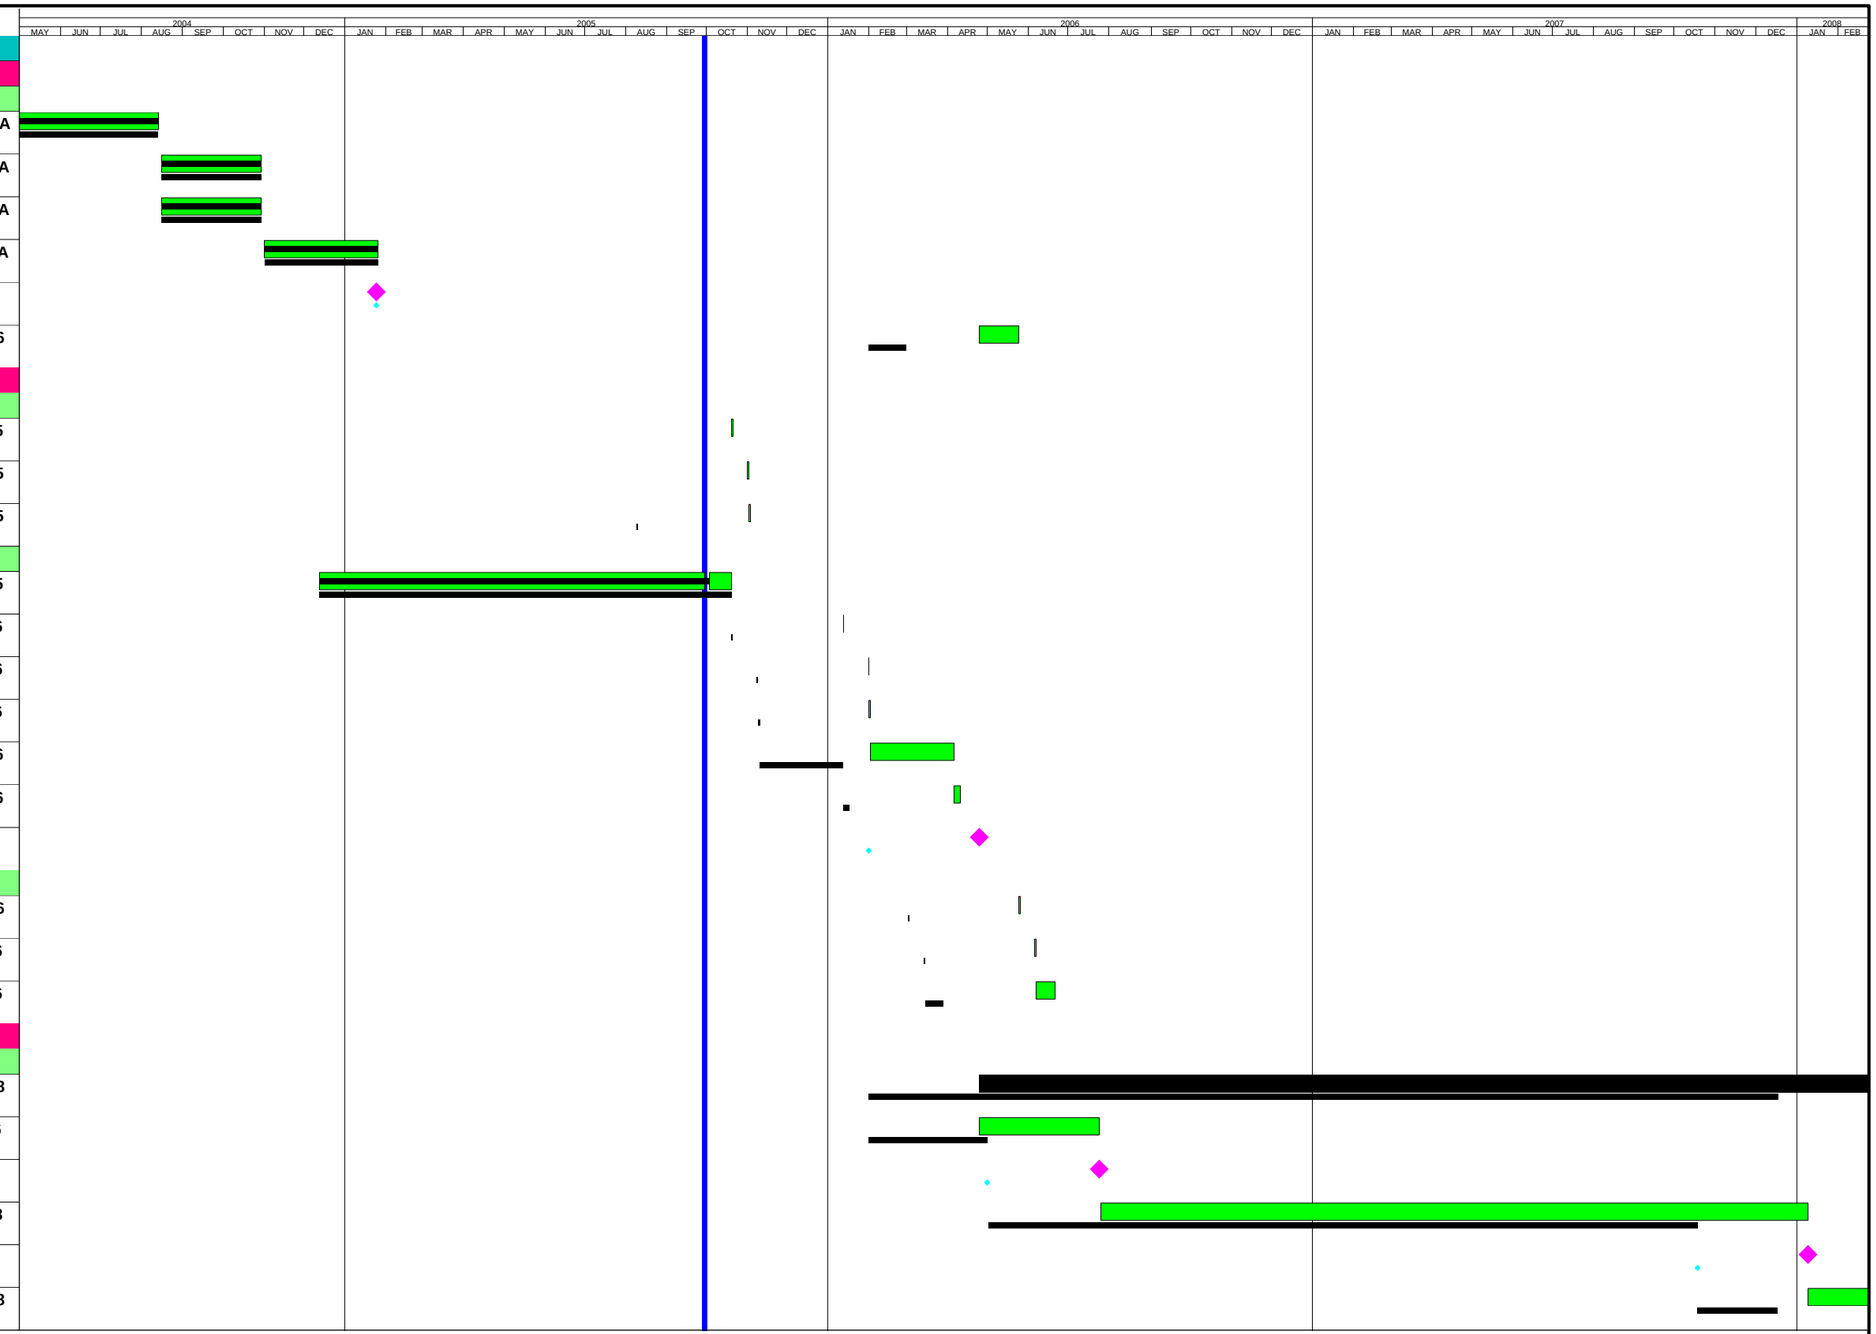

URS

COUNTY OF LOS ANGELES CALIFORNIA

© Primavera Systems, Inc.

SB1953

Project Update
OLIVE VIEW - UCLA

by S. Pogact

Date	Revision	Checked	Approved
13OCT05	September '05 update (30SEP05)		
28SEP05	August '05 update (31AUG05)		
25AUG05	July '05 update (31JUL05)		
02AUG05	June update (30JUN05)		
23JUN05	May update (31MAY05)		
