TASK	DAYS	START	FINISH
Olive View - UCLA			
AGENCY APPROVAL - PLAN CHECK			
OSHPD Plan Check Review	0	19FEB04A	13AUG04A
A&E Incorporate OSHPD comments	0*	16AUG04A	29OCT04A
A&E Incorporate NPC3 Areas.	0*	16AUG04A	29OCT04A
OSHPD Backcheck	0	01NOV04A	25JAN05A
OSHPD Stamp Approval	0	25JAN05A	
OSHPD Construction Permit	21	23MAY06	20JUN06
BID & AWARD			
B.o.S.#1 (Adopt 90% CDs)			
File, Adopt & Advertise Board Letter	1	10NOV05*	10NOV05
Board Action	1	22NOV05	22NOV05
Advertise Project	1	23NOV05	23NOV05
B.o.S.#2 (Pre-Qual., 100% CDs, Conslt. Cont.)			
AED to Prepare General Conditions for Bid	29	13DEC04A	19DEC05
File, Adopt & Adv. Approved Dwgs. & Cont. list	1	09FEB06	09FEB06
Board Action	1	28FEB06	28FEB06
Announce Final Qualified Contractor's List	1	01MAR06	01MAR06
Construction Bid Period	36	02MAR06	03MAY06
Evaluate Bids	2	04MAY06	08MAY06
Issue NTP (Consultant Agreement)	0	23MAY06	
B.o.S.#3 (Award Construction Contract)			
File / Award Board Letter	1	22JUN06	22JUN06
Board Action	1	11JUL06	11JUL06
Award & Execute Contract	8	12JUL06	25JUL06
CONSTRUCTION			
CONSTRUCTION (overall phase)	686*	23MAY06	07APR08
Consultant Agreement Work Period	90	23MAY06	20AUG06
Issue NTP (Construction)	0	21AUG06	
Construction Work (current plan)	534	22AUG06	06FEB08
Substantial Completion	0	07FEB08	
Punchlist & Project Close-out	61	07FEB08	07APR08

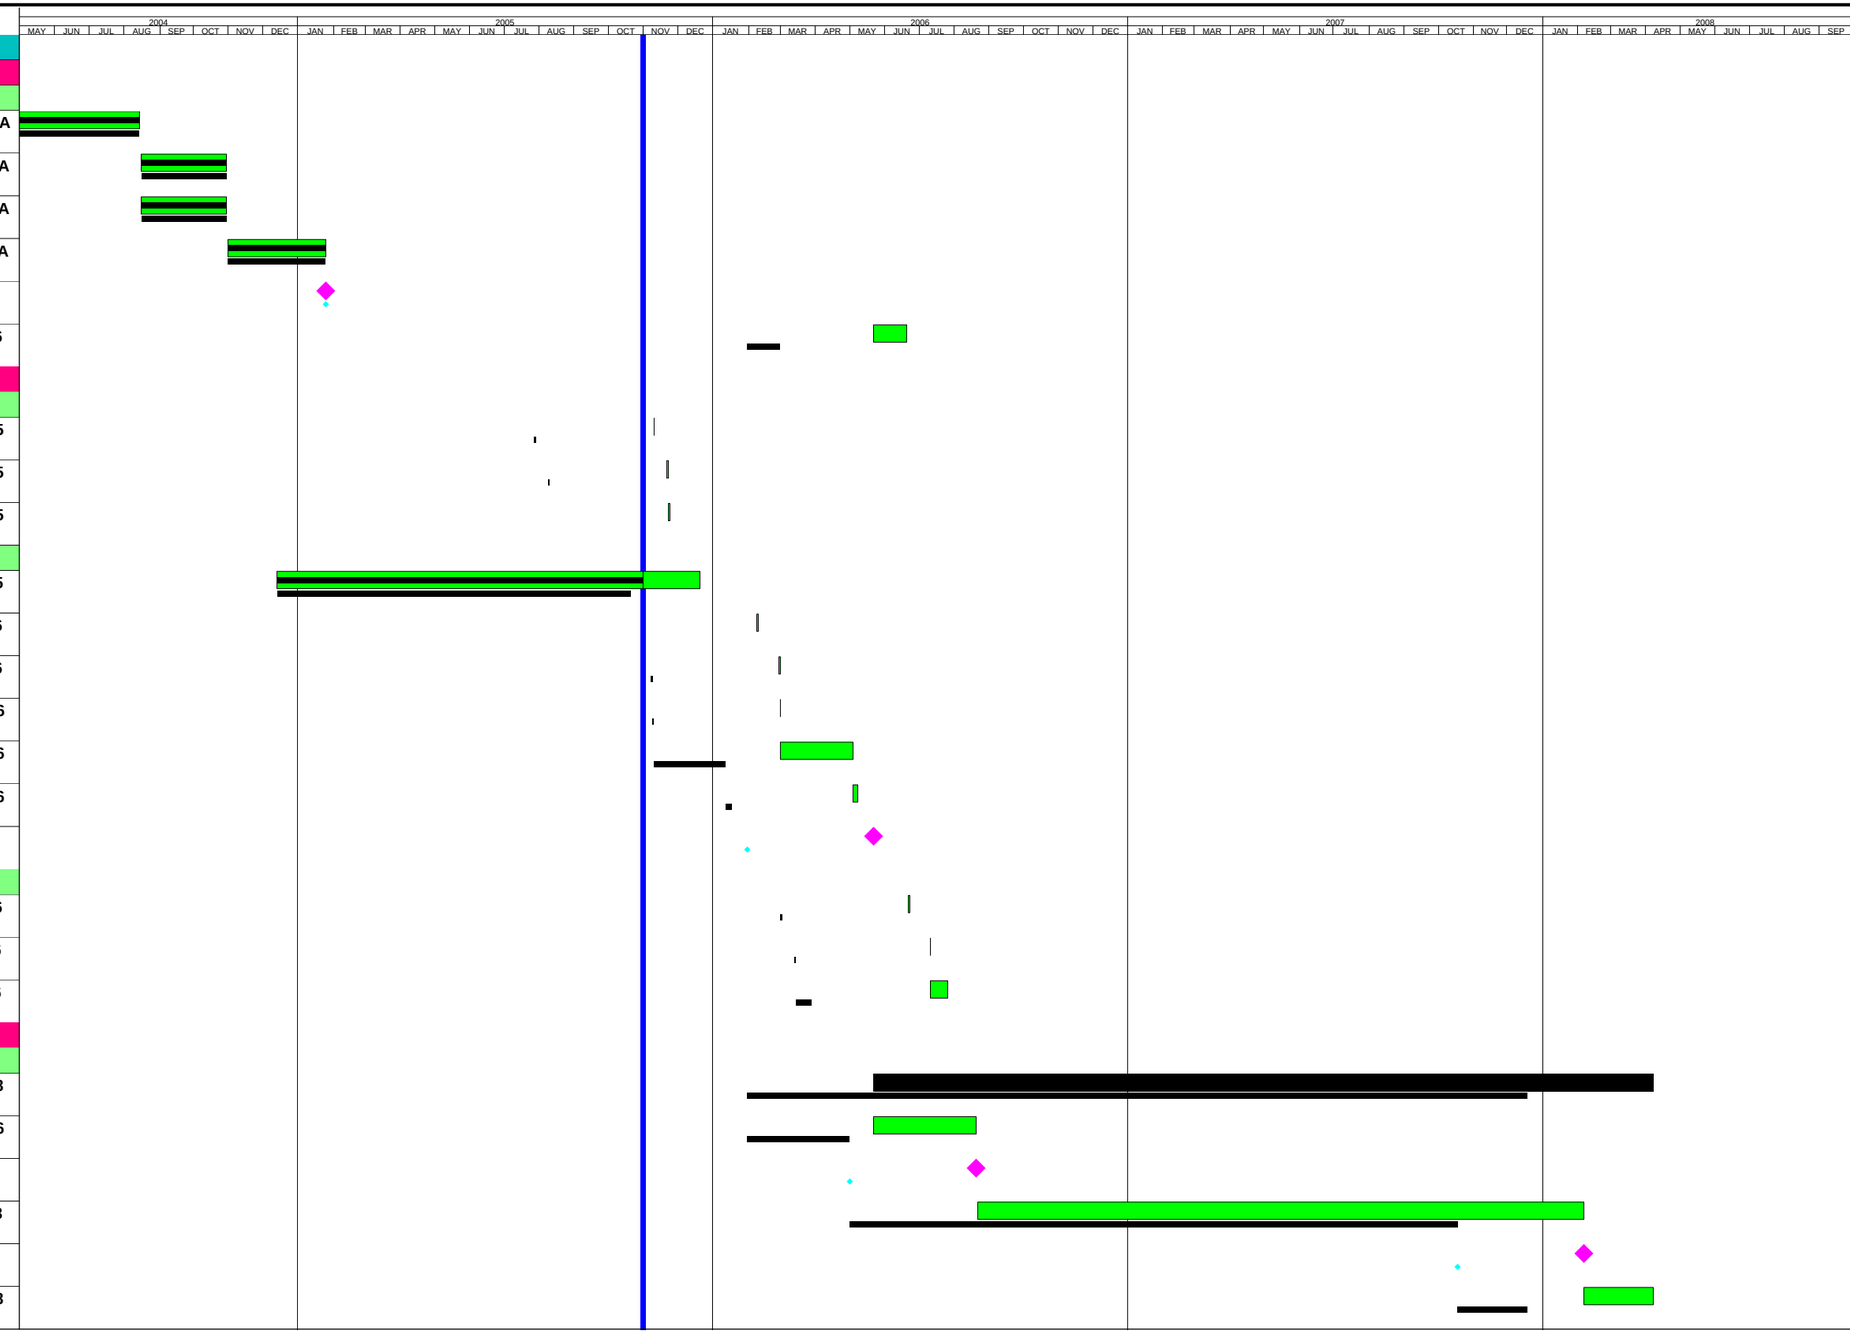

URS

© Primavera Systems, Inc.

SB1953

Project Update
OLIVE VIEW - UCLA

by S. Pogact

Date	Revision	Checked	Approved
17NOV05	October '05 update (31OCT05)		
13OCT05	September '05 update (30SEP05)		
28SEP05	August '05 update (31AUG05)		
25AUG05	July '05 update (31JUL05)		
02AUG05	June update (30JUN05)		
23JUN05	May update (31MAY05)		
