TASK	DAYS	START	FINISH
Olive View - UCLA			
AGENCY APPROVAL - PLAN CHECK			
OSHPD Plan Check Review	0	19FEB04A	13AUG04A
A&E Incorporate OSHPD comments	0*	16AUG04A	29OCT04A
A&E Incorporate NPC3 Areas.	0*	16AUG04A	29OCT04A
OSHPD Backcheck	0	01NOV04A	25JAN05A
OSHPD Stamp Approval (w/ 1yr ext)	0	25JAN05A	
OSHPD Construction Permit	21	24OCT06	21NOV06
BID & AWARD			
B.o.S.#1 (Adopt 90% CDs)			
File, Adopt & Advertise Board Letter	0	06APR06A	06APR06A
Board Action	0	18APR06A	18APR06A
Advertise Project	0	19APR06A	19APR06A
B.o.S.#2 (Pre-Qual., 100% CDs, Conslt. Cont.)			
AED to Prepare General Conditions for Bid	13	13DEC04A	21JUN06
File, Adopt & Adv. Approved Dwgs. & Cont. list	1	13JUL06	13JUL06
Board Action	1	01AUG06*	01AUG06
Announce Final Qualified Contractor's List	1	02AUG06	02AUG06
Construction Bid Period	33	03AUG06	28SEP06
Evaluate Bids	5	02OCT06	09OCT06
Issue NTP (Consultant Agreement)	0	24OCT06	
B.o.S.#3 (Award Construction Contract)			
File / Award Board Letter	1	23NOV06*	23NOV06
Board Action	1	12DEC06	12DEC06
Award & Execute Contract	8	13DEC06	27DEC06
CONSTRUCTION			
CONSTRUCTION (overall phase)	690*	24OCT06	14SEP08
Consultant Agreement Work Period	91	24OCT06	23JAN07
Issue NTP (Construction)	0	24JAN07	
Construction Work (current plan)	537	25JAN07	15JUL08
Substantial Completion	0	16JUL08	
Punchlist & Project Close-out	61	16JUL08	14SEP08

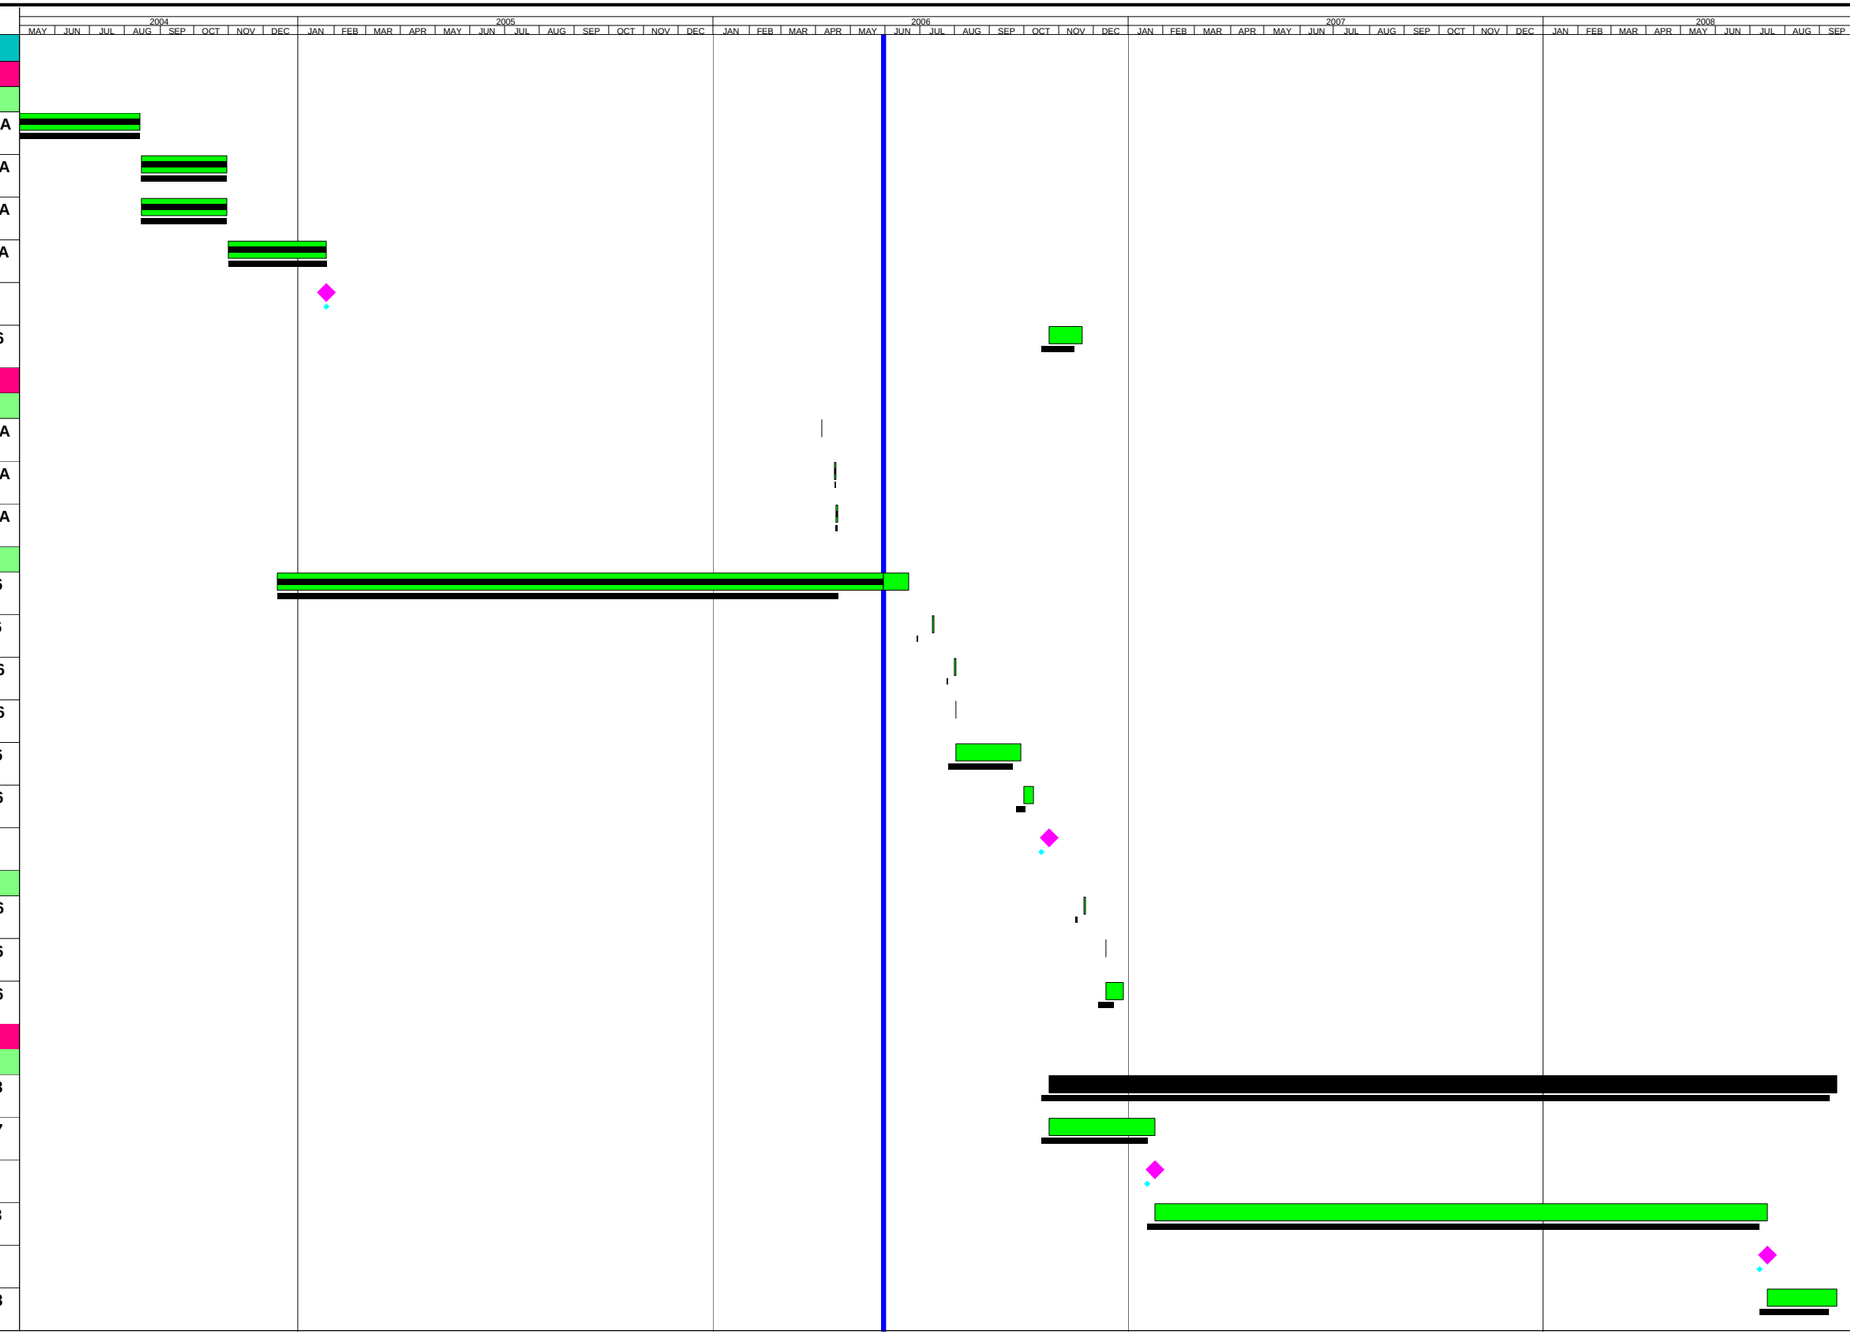

URS

COUNTY OF LOS ANGELES CALIFORNIA

© Primavera Systems, Inc.

SB1953

Project Update
OLIVE VIEW - UCLA

by S. Pogact

Date	Revision	Checked	Approved
22JUN06	May '06 update (31MAY06)		
23MAY06	April '06 update (30APR06)		
24APR06	March '06 udpate (31MAR06)		
21MAR06	February '06 update (28FEB06)		
23FEB06	January '06 update (31JAN06)		
23JAN06	December '05 update (31DEC05)		
20DEC05	November '05 update (30NOV05]		
17NOV05	October '05 update (31OCT05)		
