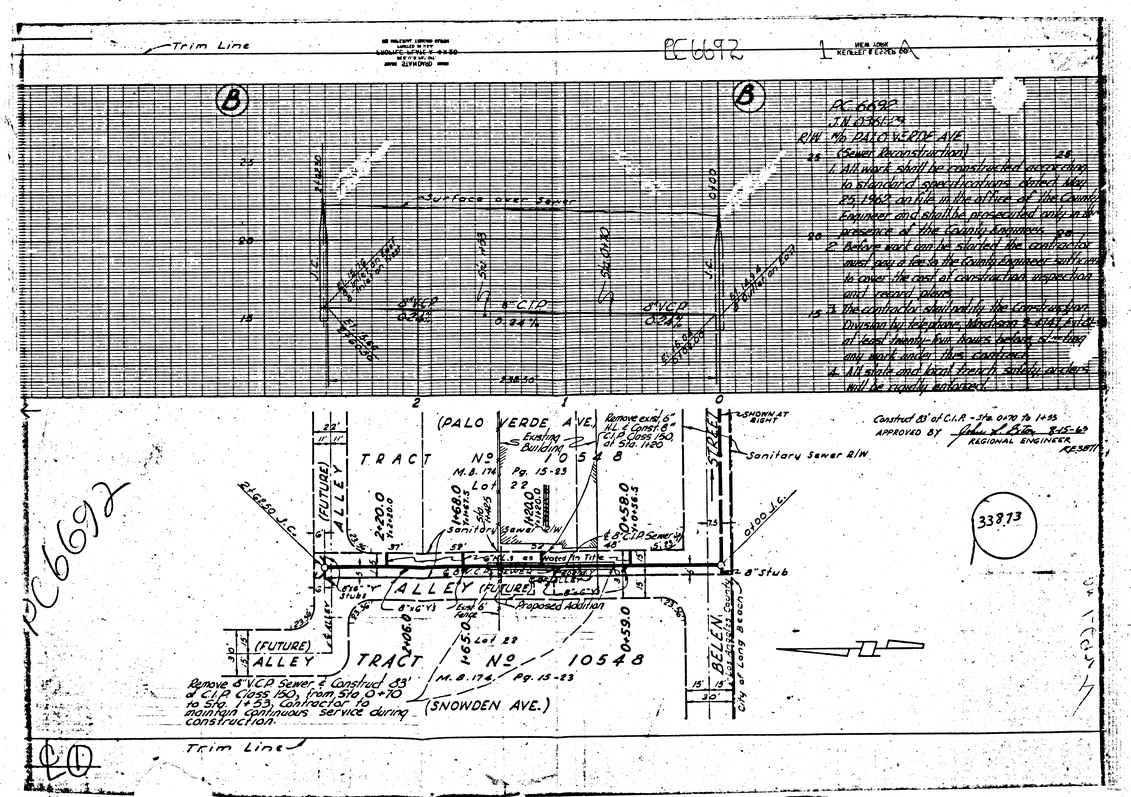
Trim Line
PC 6692
1
PC 6692
I.N 036/63
R/W No. PALO VERDE AVE.
(Sewer Reconstruction)
1. All work shall be constructed in accordance to standard specifications dated May 25, 1962 on file in the office of the County Engineer and shall be prosecuted only in the presence of the County Engineer.
2. Before work can be started the contractor must pay a fee to the County Engineer sufficient to cover the cost of construction inspection and record taking.
3. The contractor shall notify the Construction Division by telephone, Whittier 3-6141, extension 2, at least twenty-four hours before starting any work under this contract.
4. All state and local trench safety orders will be rigidly enforced.
(PALO VERDE, AVE.)
Existing Building
TRACT No. 10548
M.B. 174 Pg. 15-23
Lot 22
Remove exist'g 6" M.C. & Const'd 8" C.I.P. Class 150 at Sta. 1+20
Sanitary Sewer R/W
Const'd 8" C.I.P. Sewer
Proposed Addition
(FUTURE) ALLEY
(SNOWDEN AVE.)
Remove & Construct 8" V.C.P. Sewer & Construct 8" C.I.P. Class 150, from Sta. 0+70 to Sta. 1+53. Contractor to maintain continuous service during construction.
Construct 8" C.I.P. - Sta. 0+70 to 1+53
APPROVED BY
REGIONAL ENGINEER
8-15-63
338.73
Trim Line
PC 6692
