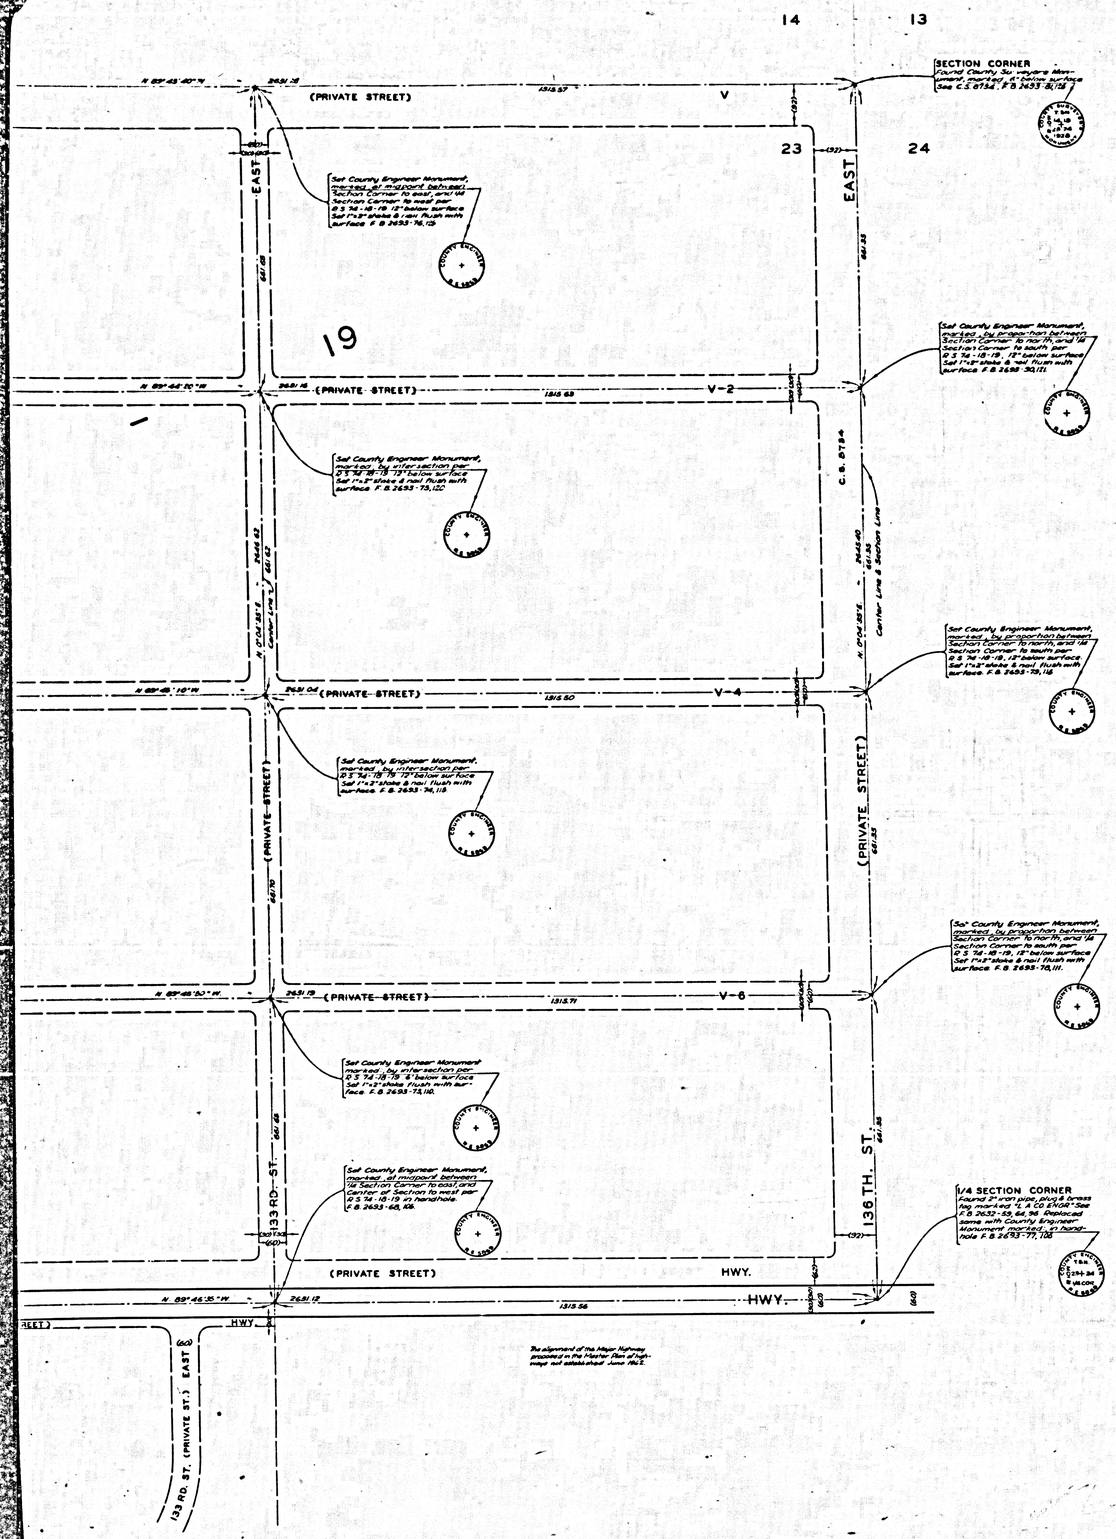

COUNTY OF LOS ANGELES
MAP OF

WATER WORKS DISTRICT NO. 24
STREETS IN R. S. 74 - 18 - 19

COUNTY SURVEYORS MAP NO. B-2782
SCALE: 1 INCH = 100 FT.

JOB NUMBER 0021.60

JOHN A. LAMBIE - COUNTY ENGINEER
SURVEYED MARCH 1961

SURVEYED UNDER INSTRUCTIONS OF THE BOARD OF SUPERVISORS PER ORDER DATED JUNE 4, 1957

BEARINGS ARE BASED ON THE BEARING OF WEST SECTION LINE OF SEC. 23 T.5N., R.10W. FROM E. 1/4 CORNER NORTH TO THE SECTION CORNER OF SEC. 15, 14, 22, 23 AS SHOWN ON C.S.B. 2568-1

F.B. 2693 - 55 - 128

FIELD WORK BY ..... S. HALISCKY
OFFICE WORK BY ..... G.O. HARRIS
CHECKED BY ..... H.E. AUSTIN
..... J. AJA

Revised April, 1961 - J.A.L.

I.M. 66

CSB-2782
A1 OF A2

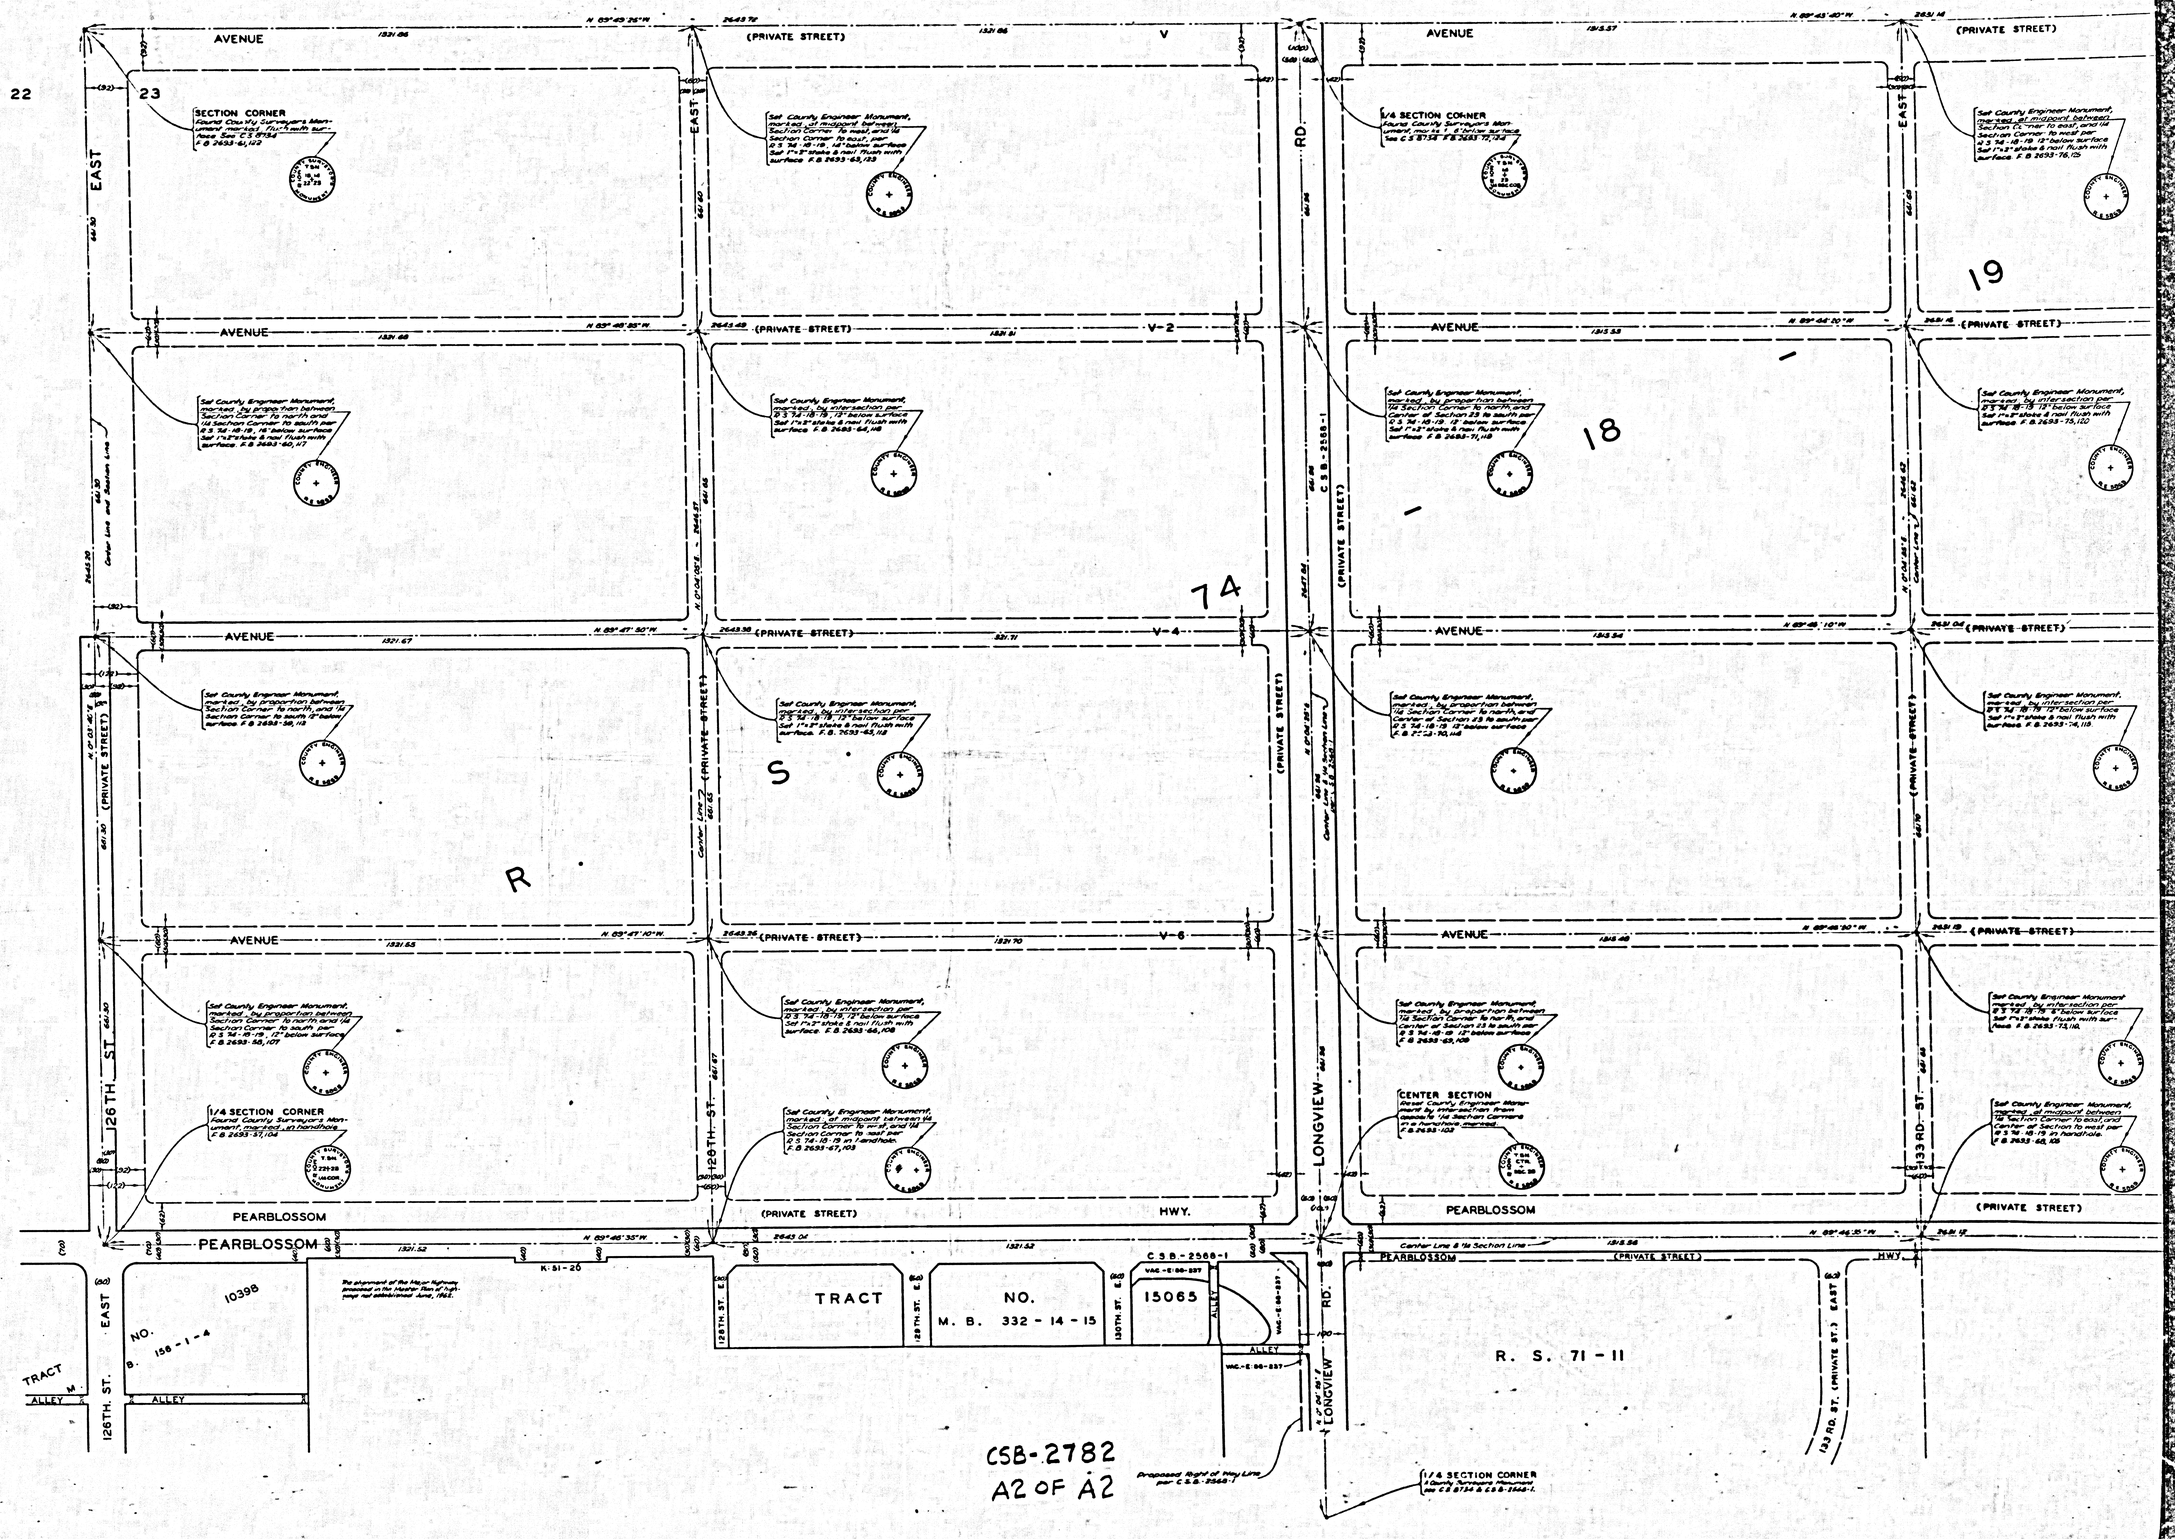
15
14
22
23
19
18
74
S
R
AVENUE
(PRIVATE STREET)
V
V-2
V-4
V-6
EAST
RD.
SECTION CORNER
Found County Surveyor's Monument marked flush with surface. See C.S. 8734
F.B. 2693-61,112
1/4 SECTION CORNER
Found County Surveyor's Monument marked, in handhole
F.B. 2693-33,104
CENTER SECTION
Found County Engineer Monument marked by intersection from opposite 1/4 Section Corners
F.B. 2693-103
Set County Engineer Monument, marked, by intersection per 0.S.74-18-19, 12" below surface
Set 1"x2" stake & nail flush with surface. F.B. 2693-65,118
Set County Engineer Monument, marked, by intersection per 0.S.74-18-19, 12" below surface
Set 1"x2" stake & nail flush with surface. F.B. 2693-76,120
Set County Engineer Monument, marked, by intersection per 0.S.74-18-19, 12" below surface
Set 1"x2" stake & nail flush with surface. F.B. 2693-58,101
Set County Engineer Monument, marked, at midpoint between 1/4 Section Corner to north and 1/4 Section Corner to south per 0.S.74-18-19, 12" below surface
F.B. 2693-66,108
Set County Engineer Monument, marked, at midpoint between 1/4 Section Corner to north and 1/4 Section Corner to south per 0.S.74-18-19 in handhole
F.B. 2693-47,103
Set County Engineer Monument, marked, by projection between 1/4 Section Corner to north and 1/4 Section Corner to south per 0.S.74-18-19, 12" below surface
Set 1"x2" stake & nail flush with surface. F.B. 2693-36,118
Set County Engineer Monument, marked, by projection between 1/4 Section Corner to north and Center of Section 23 to south per 0.S.74-18-19, 12" below surface
Set 1"x2" stake & nail flush with surface. F.B. 2693-71,118
Set County Engineer Monument, marked, by projection between 1/4 Section Corner to north and Center of Section 23 to south per 0.S.74-18-19, 12" below surface
F.B. 2693-70,118
Set County Engineer Monument, marked, at midpoint between 1/4 Section Corner to north and Center of Section 23 to south per 0.S.74-18-19, 12" below surface
Set 1"x2" stake & nail flush with surface. F.B. 2693-63,109
Set County Engineer Monument, marked, at midpoint between 1/4 Section Corner to north and Center of Section 23 to south per 0.S.74-18-19 in handhole
F.B. 2693-60,105
Set County Engineer Monument, marked, by intersection per 0.S.74-18-19, 12" below surface
Set 1"x2" stake & nail flush with surface. F.B. 2693-15,110
Set County Engineer Monument, marked, by intersection per 0.S.74-18-19, 12" below surface
Set 1"x2" stake & nail flush with surface. F.B. 2693-14,118
Set County Engineer Monument, marked, by intersection per 0.S.74-18-19, 12" below surface
Set 1"x2" stake & nail flush with surface. F.B. 2693-12,114
126TH. ST.
129TH. ST.
133RD. ST.
LONGVIEW
PEARBLOSSOM
HWY.
K-51-26
TRACT
NO.
M. B. 332-14-15
C.S.B.-2568-1
15065
ALLEY
VAC.-E-86-237
10398
NO.
B. 156-1-4
R. S. 71-11
CSB-2782
A2 OF A2
Proposed Right of Way Line per C.S.B.-2568-1
1/4 SECTION CORNER
County Surveyors Monument
See C.S. 8734 & C.S.B.-2568-1.
